

Liddell Road, West Hampstead - **Construction Working Group** – 22nd February 2024



Agenda

1. Brief introductions
2. Presentation
3. Q&A

Actions / Concerns that were raised since the last CWG Meeting

Task: To upload the latest monitoring reports for noise, dust and vibrations onto the project website.

Action: This action was completed by Cavendish, and all materials have been circulated with the CWG via the project website.

Task: Provide an update on the delivery of the next round of car washing vouchers for the effected residents.

Action: The final batch of car washing vouchers have been made available for collection and have been informed by the project team.

Task: Organize for a cleaning vehicle to attend Maygrove Road and clean any excess mess off the road.

Action: The project team organized for a cleaning truck to attend the site on two occasions in February, with the most recent occasion being on Tuesday 20th February.

Monitoring Station Locations

Dust Monitor 3
Noise Monitor

Vibration Monitor
Network rail


Monitoring Stations – MCERT Real Time
Monitor specification to comply with BS
Standard

Dust monitor 2

Noise and Vibration
Monitor

Noise and Vibration
Monitor Block A

Dust Monitor 1

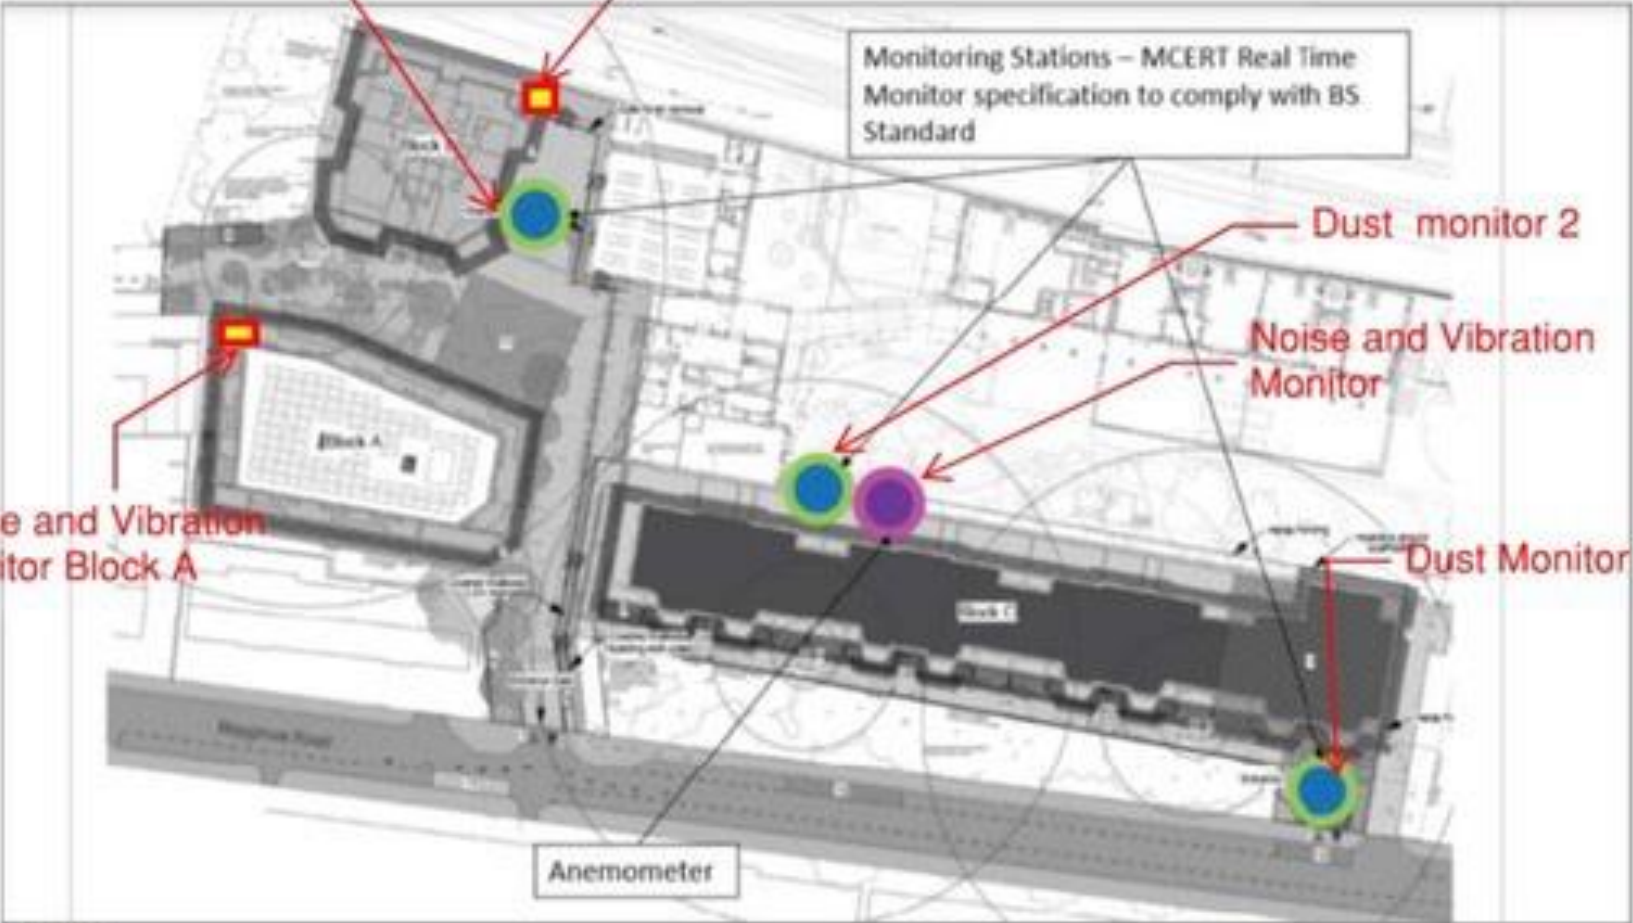

Anemometer

Figure 1

Noise and Vibration Statistics for January

Position 2: There were no noise exceedances for Position 2 throughout the course of January 2024.

Position 3: There were no noise exceedances for Position 3 throughout the course of January 2024.

Note: Monitoring stations have now been reduced due to the area handover.

Noise and Vibration Statistics for Position 2

Day	Date	Total noise level L _{Aeq,T} dB	Noise level averaging time	Noise Exceedance	Reason & Action
Mon	01.01.24	62.3	10hr	No	
Tues	02.01.24	63.0	10hr	No	
Wed	03.01.24	64.4	10hr	No	
Thurs	04.01.24	69.3	10hr	No	
Fri	05.01.24	63.4	10hr	No	
Sat	06.01.24	*	5hr	No	Hoarding Monitor on being taken down
Mon	08.01.24	*	10hr	No	
Tues	09.01.24	*	10hr	No	
Wed	10.01.24	*	10hr	No	
Thurs	11.01.24	*	10hr	No	
Fri	12.01.24	*	10hr	No	
Sat	13.01.24	*	5hr	No	
Mon	15.01.24	*	10hr	No	
Tues	16.01.24	*	10hr	No	
Wed	17.01.24	*	10hr	No	
Thurs	18.01.24	*	10hr	No	
Fri	19.01.24	*	10hr	No	
Sat	20.01.24	*	5hr	No	
Mon	22.01.24	*	10hr	No	
Tues	23.01.24	*	10hr	No	
Wed	24.01.24	*	10hr	No	
Thurs	25.01.24	*	10hr	No	
Fri	26.01.24	*	10hr	No	
Sat	27.01.24	*	5hr	No	
Mon	29.01.24	*	10hr	No	
Tues	30.01.24	*	10hr	No	
Wed	31.01.24	*	10hr	No	

Noise and Vibration Statistics for Position 3

Day	Date	Total noise level L _{Aeq,T} dB	Noise level averaging time	Noise Exceedance	Reason & Action
Mon	01.01.24	34.5	10hr	No	
Tues	02.01.24	39.4	10hr	No	
Wed	03.01.24	37.5	10hr	No	
Thurs	04.01.24	34.8	10hr	No	
Fri	05.01.24	35.2	10hr	No	
Sat	06.01.24	35.7	5hr	No	
Mon	08.01.24	37.0	10hr	No	
Tues	09.01.24	33.1	10hr	No	
Wed	10.01.24	33.6	10hr	No	
Thurs	11.01.24	31.0	10hr	No	
Fri	12.01.24	28.6	10hr	No	
Sat	13.01.24	31.4	5hr	No	
Mon	15.01.24	31.1	10hr	No	
Tues	16.01.24	29.1	10hr	No	
Wed	17.01.24	31.7	10hr	No	
Thurs	18.01.24	30.3	10hr	No	
Fri	19.01.24	32.5	10hr	No	
Sat	20.01.24	34.5	5hr	No	
Mon	22.01.24	33.4	10hr	No	
Tues	23.01.24	32.2	10hr	No	
Wed	24.01.24	33.9	10hr	No	
Thurs	25.01.24	31.4	10hr	No	
Fri	26.01.24	32.4	10hr	No	
Sat	27.01.24	32.2	5hr	No	
Mon	29.01.24	31.0	10hr	No	
Tues	30.01.24	31.2	10hr	No	
Wed	31.01.24	29.9	10hr	No	

Summary of Dust Statistics for January

Week/commencing	Max ug/m ³	Min ug/m ³	Average ug/m ³	15min Alert>170 ug/m ³	15min Action Level >250ug/m ³	Ave 1 Hour Action Level>190ug/m ³	Data Capture %
01.01.24 - 06.01.24	300.0	4.4	37.8	2	1	0	100
08.01.24 - 13.01.24	*	*	*	*	*	*	0
15.01.24 - 20.01.24	*	*	*	*	*	*	0
22.01.24 - 31.01.24	*	*	*	*	*	*	0

Summary:

Position 3 had no exceedances of the 190ug/m³ Trigger Level throughout the month of January 2024.

Note: Monitoring stations have now been reduced due to the area handover.

Monthly Look Ahead – February to March 2024

Block A – Low Noise Level

Internal works ongoing for Block A

Hard landscaping works around Block A

Soft landscaping works around Block A

Block B – Low Noise Level

Internal Works ongoing for Block B

Hard landscaping works around Block B

Soft landscaping works around Block B

Block C – Low Noise Level

Block C was handed over in February 2024

Liddell Road, West Hampstead - Construction Working Group – 21st March 2024

